

**RICHLAND COUNTY GOVERNMENT  
UTILITIES DEPARTMENT**

7525 Broad River Road, Irmo, SC 29063  
T 803-401-0050 | F 803-401-0030  
rcu\_services@richlandcountysc.gov | richlandcountysc.gov



**MEMORANDUM**

**TO:** The Honorable Cheryl English, Richland County Council, District 10  
The Honorable Chakisse Newton, Richland County Council, District 11

**FROM:** Bill Davis, Director of Utilities  
John M. Thompson, Ph.D., MBA, CPM, Assistant County Administrator

**Date:** October 15, 2021

**Subject:** Southeast Richland County Sewer & Water Systems Expansion Project Update

**CC:** Leonardo Brown, MBA, CPM, County Administrator

**Project Construction Update**

The Southeast Richland County Sewer & Water Systems Expansion Project construction continues per design. The information sometimes will look repeated since it is along a stretch of road in a tranquil country setting and staff anticipates that there should not be any barriers to impede progress. The project work continues at a good pace for all the divisions. The report is updated with new photos captured for the project work.

All four divisions of Phase 1 are in construction. The weekly report will provide updates on the progress of each division. The design shows the lines along Lower Richland Boulevard, Airbase Road, Congaree Road, Bluff Road, Reynolds Road, Cabin Creek Road, Ault Road, Trotter Road, Congaree Church Road, and Clarkson Road. The project status will also include the construction of sewer lines, water lines, lift stations, water service connections, and sewer service connections along the routes.

We have listed the Contract completion dates below. These dates do not reflect any adjustments for rain, equipment, and material delivery delays (due to COVID -19). The delays will be monitored and the timeline will be adjusted with each report. The current Division 1, Division 2, and Division 2B substantial completion dates are January 10, 2021, with final completion on February 9, 2021. Division 3 and Division 3B substantial completion dates are January 26, 2021, with final completion February 25, 2021. The Division 4 substantial completion date is March 7, 2021, with final completion April 6, 2021.

**RICHLAND COUNTY GOVERNMENT  
UTILITIES DEPARTMENT**

7525 Broad River Road, Irmo, SC 29063  
T 803-401-0050 | F 803-401-0030  
rcu\_services@richlandcountysc.gov | richlandcountysc.gov



**DIVISION 1**

Last week, one crew tied the McEntire pump station to the force main and worked on the pump station piping (90% complete). A second crew worked on general items such as installing Valve protector rings, pipeline markers and grouting air/vacuum valve manholes. A third crew worked on site grading at the Garners Ferry lift station site, tie in of the Garners Ferry Road lift station to the force main and the electrician worked on the Garners Ferry Road lift station. Next week the electrician will work on setting the control panel at the McEntire lift station and electrical work at the Garners Ferry Road lift station. A second crew will work on punch list items and clean-up.

Installed as of October 7, 2021	Installed week of October 7, to October 14, 2021	Total installed to date	Percent complete
FM 59,549 Feet	0 Feet	59,549 Feet	100.0%
Water 32,083 Feet	0 Feet	32,083 Feet	100.0%

The crew installing McEntire wetwell. (See photo 1). The crew will have a no flagger. Forty-six (46) out of forty-six (46) fire hydrants installation completed in Division 1.



Photo 1: McEntire wetwell

**RICHLAND COUNTY GOVERNMENT  
UTILITIES DEPARTMENT**

7525 Broad River Road, Irmo, SC 29063  
T 803-401-0050 | F 803-401-0030  
rcu\_services@richlandcountysc.gov | richlandcountysc.gov



**DIVISION 2**

Last week all work was complete at the Gadsden lift station. Next week one crew will continue to wrap up any punch list items for Division 2 and the fence crew will install the fence at the Gadsden lift station.

Installed as of October 7, 2021	Installed week of October 7, to October 14, 2021	Total installed to date	Percent complete
FM 50,000 Feet	0 Feet	50,000 Feet	100.0%
Water 28,880 Feet	0 Feet	28,880 Feet	100.0%

The crew installed control panel. (See photo 2). The crew will have a no flagger. Forty-three (43) out of forty-three (43) fire hydrants installation completed in Division 2.



Photo 2: Control Panel



**RICHLAND COUNTY GOVERNMENT  
UTILITIES DEPARTMENT**

7525 Broad River Road, Irmo, SC 29063  
T 803-401-0050 | F 803-401-0030  
rcu\_services@richlandcountysc.gov | richlandcountysc.gov



**DIVISION 3**

The majority of the work is complete until the new lift stations can be tested and tied to the force main that delivers the wastewater to the Eastover Wastewater Treatment Plant. The Crew mobilized and are ready to do the bores under the Railroad. Next week, the crews will begin bores under the Railroad. The Division 3 office staff is now back from COVID quarantine, and their office is now open.

Installed as of October 7, 2021	Installed week of October 7, to October 14, 2021	Total installed to date	Percent complete
FM 61,950 Feet	0 Feet	61,950 Feet	99.9%
Water 21,150 Feet	0 Feet	21,150 Feet	99.9%

The contractor installing water connection. (See photo 3). There is no flagger expected for traffic. Twenty-six (26) out of twenty-six (26) fire hydrants installation completed in Division 3.

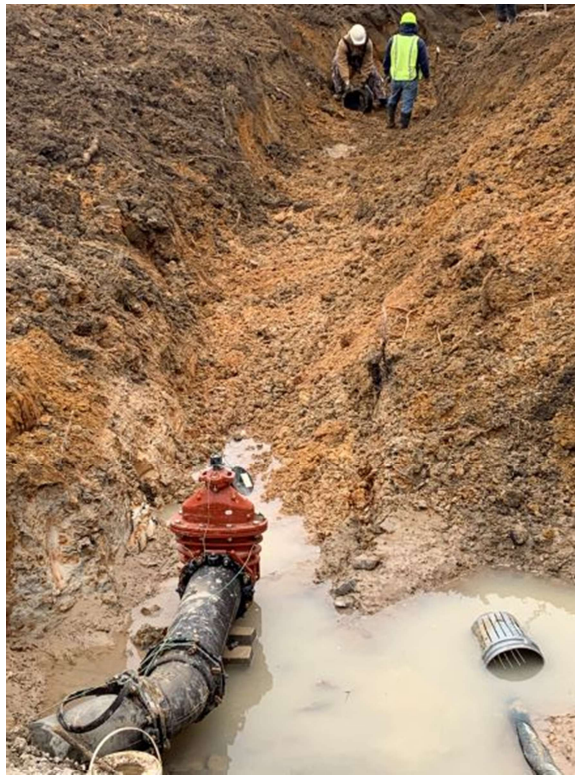


Photo 3: Water Tap



**RICHLAND COUNTY GOVERNMENT  
UTILITIES DEPARTMENT**

7525 Broad River Road, Irmo, SC 29063  
T 803-401-0050 | F 803-401-0030  
rcu\_services@richlandcountysc.gov | richlandcountysc.gov



**DIVISION 4**

The majority of the work is complete until the new lift stations can be tied to the force main that delivers the wastewater to the Eastover Wastewater Treatment Plant.

Installed as of October 7, 2021	Installed week of October 7, to October 14, 2021	Total installed to date	Percent complete
FM 13,470 Feet	0 Feet	13,470 Feet	100.0%
Gravity 1,500 Feet	0 Feet	1,500 Feet	100.0%

The line valve installation (See photo 4). There will be no flagger required next week. There are no water lines installed and no fire hydrants designed in Division 4.



Photo 4: Valve pit

